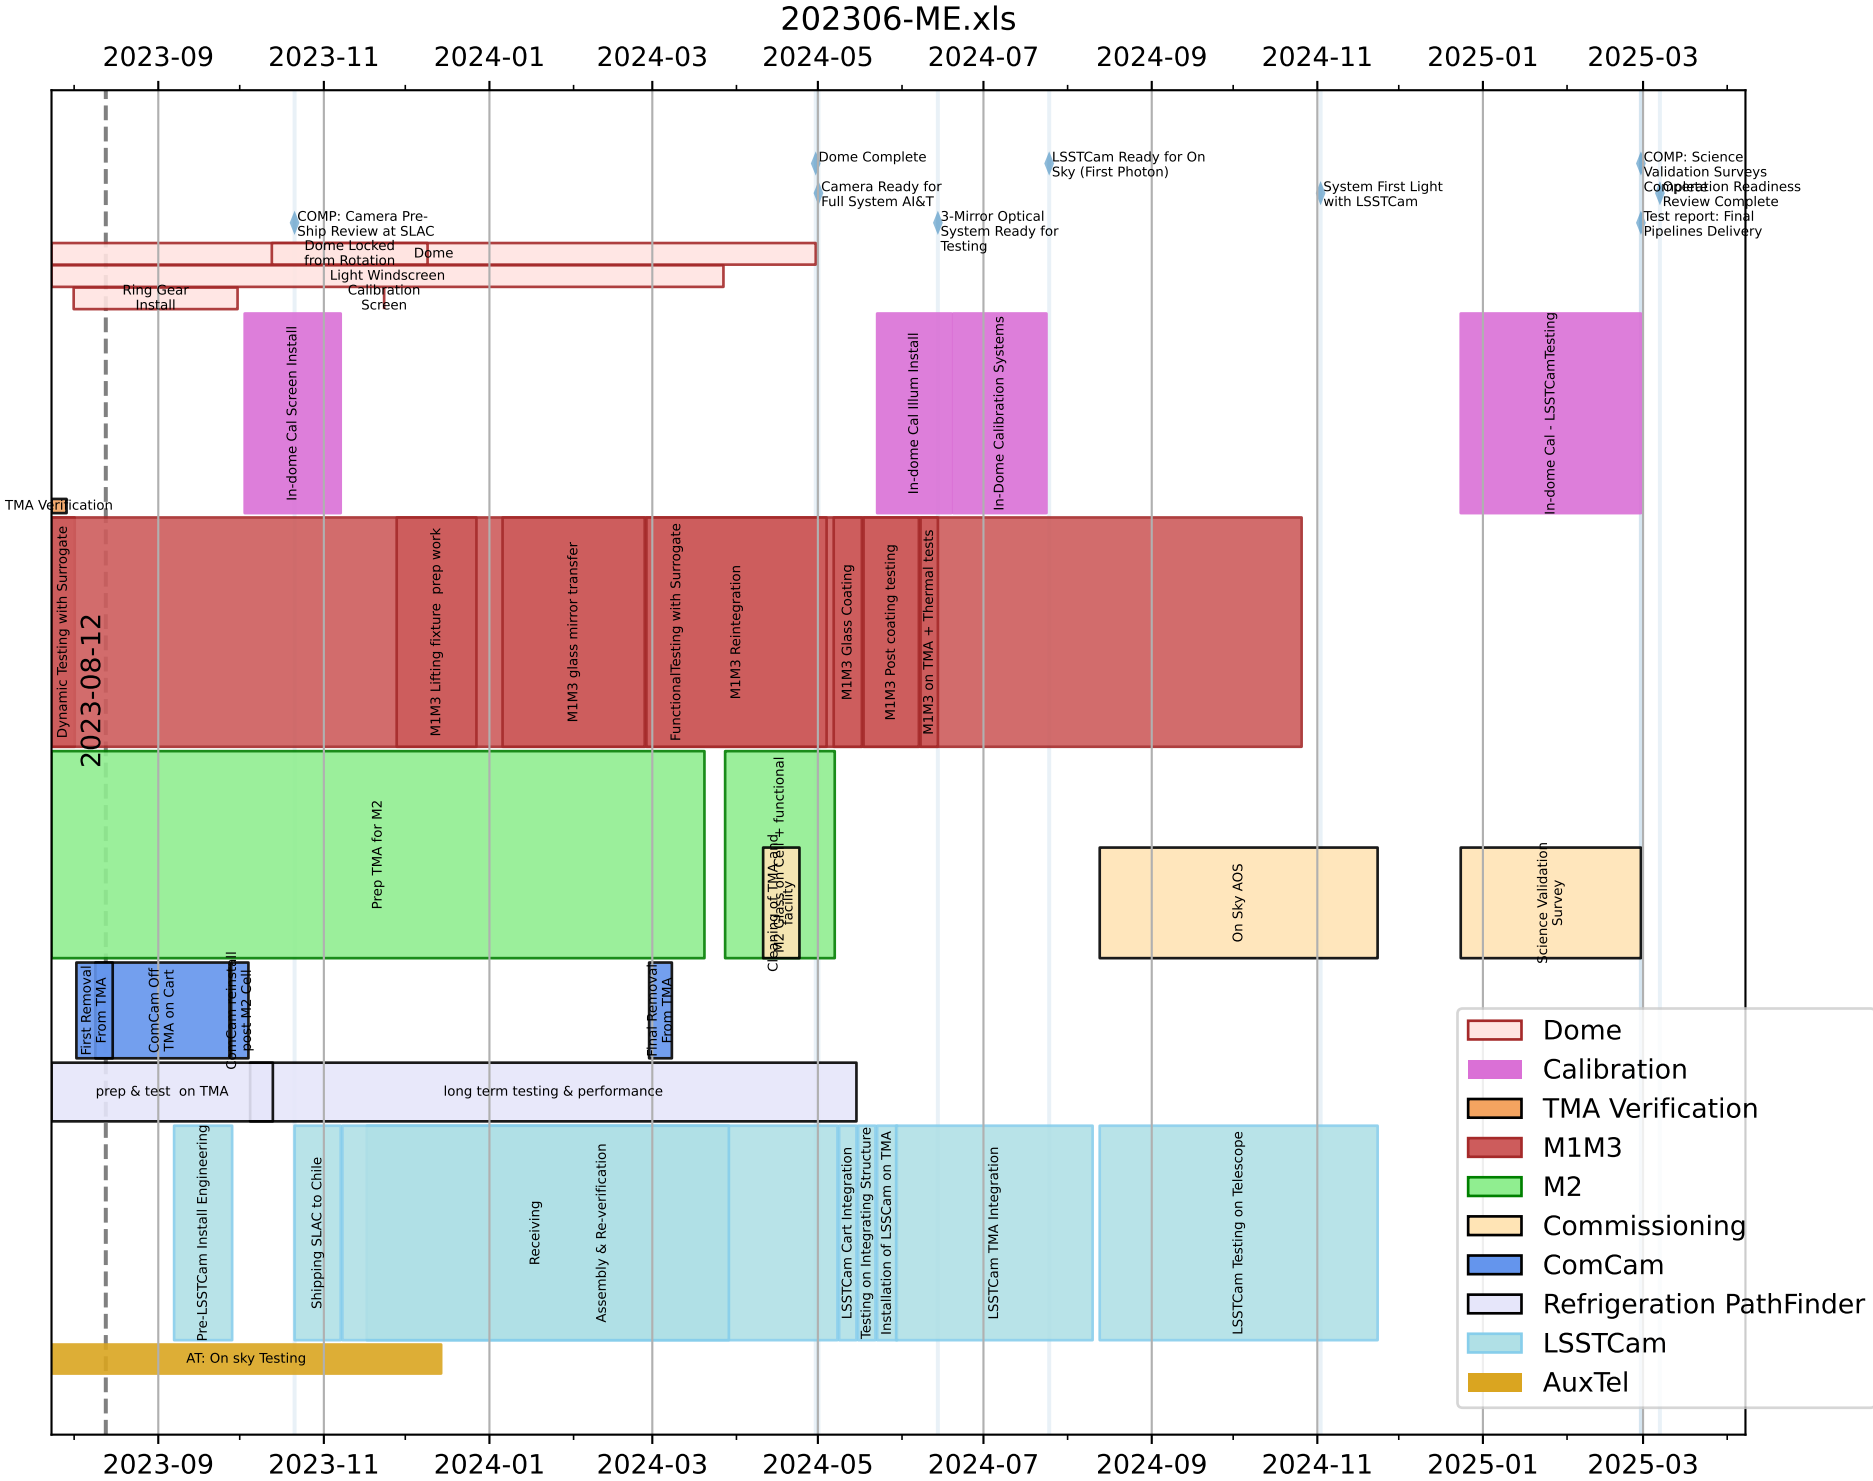
202306-ME.xls
2023-09
2023-11
2024-01
2024-03
2024-05
2024-07
2024-09
2024-11
2025-01
2025-03
Dome Complete
Camera Ready for Full System AI&T
LSSTCam Ready for On Sky (First Photon)
System First Light with LSSTCam
COMP: Science Validation Surveys Complete
Operation Readiness Review Complete
Test report: Final Pipelines Delivery
COMP: Camera Pre-Ship Review at SLAC
3-Mirror Optical System Ready for Testing
Dome Locked from Rotation
Dome
Light Windscreen
Calibration Screen
Ring Gear Install
In-dome Cal Screen Install
In-dome Cal Illum Install
In-Dome Calibration Systems
In-dome Cal - LSSTCamTesting
TMA Verification
Dynamic Testing with Surrogate
2023-08-12
M1M3 Lifting fixture prep work
M1M3 glass mirror transfer
FunctionalTesting with Surrogate
M1M3 Reintegration
M1M3 Glass Coating
M1M3 Post coating testing
M1M3 on TMA + Thermal tests
Prep TMA for M2
Cleaning of TMA and M2 Cell + functional
Glass Thermal Facility
On Sky AOS
Science Validation Survey
First Removal From TMA
ComCam Off TMA on Cart
ComCam Install post M2 Cell
Final Removal From TMA
prep & test on TMA
long term testing & performance
Pre-LSSTCam Install Engineering
Shipping SLAC to Chile
Receiving
Assembly & Re-verification
LSSTCam Cart Integration
Testing on Integrating Structure
Installation of LSSCam on TMA
LSSTCam TMA Integration
LSSTCam Testing on Telescope
AT: On sky Testing
Dome
Calibration
TMA Verification
M1M3
M2
Commissioning
ComCam
Refrigeration PathFinder
LSSTCam
AuxTel
